

Van: [redacted]@odrn.nl>
Verzonden: 21-04-2021 16:51
Aan: [redacted]@odrn.nl>
CC: [redacted]@inspectieszw.nl>
Onderwerp: FW: meldingen asbestverwijdering RK1 (Hollandiaweg 11)

Hoi [redacted]

Ze zijn nog niet begonnen aan de daadwerkelijke ROI maar wel ernaast, E filters. ROI is volgens mij wel doormiddel van sloop losgekoppeld van de andere bouwdelen, maar controle moet dat uitwijzen.

En blijkbaar saneren ze het asbest (bronnen 3 en 6) in de E filters onder risicoklasse 1 terwijl we hebben aangegeven dat naar onze mening die risicoklasse niet correct is bij de bronnen. Met Bron 6 heb ik om motivatie vanuit hun kant gevraagd en bij bron 3 heb ik aangegeven dat men de SMART naar nu blijkt niet conform waarheid heeft ingevuld.

Als ze hiermee doorgaan dan moeten we hier wat mee

Met vriendelijke groet,

[redacted]

Toezichthouder | Asbestdeskundige
bereikbaar op di/wo/do/vr

Mariënborg 75, 6511 PS Nijmegen | Postbus 1603, 6501 BP Nijmegen

☎ 024- [redacted] | ✉ [redacted]@odrn.nl | 🌐 www.odregionijmegen.nl




Aangesloten bij:



N.B.

Alle per e-mail verzonden stukken die horen bij een vergunning, moet u ook via de reguliere weg indienen. Dit is per post of via het Omgevingsloket online.



Van: [redacted]@engie.com <[redacted]@engie.com>

Verzonden: woensdag 21 april 2021 15:55

Aan: [redacted]@inspectieszw.nl

CC: [redacted]@odrn.nl>; [redacted]@inspectieszw.nl; [redacted]@outlook.com;

[J]@brownandmason.com

Onderwerp: RE: meldingen asbestverwijdering RK1 (Hollandiaweg 11)

Geachte [J],

Bijgaand treft u de antwoorden aan op uw vragen d.d. 12 april 2021.

Zie hiervoor onder in rood aangegeven de antwoorden op uw vragen.

Hopende u hiermee voldoende geïnformeerd te hebben.

Met vriendelijke groet, kind regards, bien à vous,

[J]

5.1.2e 5.1.2e 5.1.2e

Generation Europe BU

European Maintenance Support EMS

[J]@engie.com

Tel : +31 [J]

GSM : +31 [J]



European

Maintenane

Support



engie.com

Grote Voort 291, 8041 BL Zwolle
Postbus 10087, 8000 GB Zwolle

Please consider the environment before printing this document.

Van: [J]@inspectieszw.nl>

Verzonden: maandag 12 april 2021 15:20

Aan: [J] (ENGIE Generation Europe) <[J]@engie.com>

CC: [J]@odrn.nl; [J]@inspectieszw.nl>; [J]@outlook.com

Onderwerp: ⚠ meldingen asbestverwijdering RK1 (Hollandiaweg 11)

Beste [J]

In ons systeem trof ik bijgevoegde twee meldingen van asbestverwijdering in risicoklasse 1 op de locatie Hollandiaweg 11 te Nijmegen. Het gaat hierbij om asbesthoudend karton (1.200 m² + 1.400 m²), die in de periode 17-2 t/m 5-3 is verwijderd en die nu wordt verwijderd.

- Om welk deel van de bebouwing gaat het hierbij? **Bouwdeel 14 E-filters.**

- Welk asbestinventarisatierapport ligt hieraan ten grondslag? Zoals in de melding reeds vermeld inventarisatierapport van de firma van Santen met projectnummer 201314.4 versie 1.0 en in later stadium 201314.4 versie 1.1 dit t.b.v het in zijn geheel verwijderen van een deel textielband.
- Op welke bronnen hebben de meldingen betrekking? Bron 3 en bron 6.
- Wie heeft de werkzaamheden uitgevoerd en wie is de werkzaamheden nu aan het uitvoeren? Brown and Mason alles in RK 1.
- Kun je resultaten van eindbeoordelingen toezenden? Zie bijlage.

Alvast bedankt voor je reactie.



Met vriendelijke groet,



Inspecteur Arbeidsomstandigheden – Asbest- en bodemdeskundige

Toeziethouder en buitengewoon opsporingsambtenaar

Inspectie SZW

Ministerie van Sociale Zaken & Werkgelegenheid

✉ @inspectieszw.nl ☎ 06-

Tel: 070 Meldingen 0800 5151 | www.inspectieszw.nl

Bezoekadres: Croeselaan 15, 3521 BJ Utrecht | Postadres: Postbus 90801, 2509 LV Den Haag |

De Inspectie SZW werkt aan eerlijk, gezond en veilig werk en bestaanszekerheid voor iedereen. Ze doet dit op basis van risico- en omgevingsanalyses. Toezicht en opsporing worden daar ingezet waar de meest hardnekkige problemen zitten en het effect het grootst is.

Dit bericht kan informatie bevatten die niet voor u is bestemd. Indien u niet de geadresseerde bent of dit bericht abusievelijk aan u is toegezonden, wordt u verzocht dat aan de afzender te melden en het bericht te verwijderen. De Staat aanvaardt geen aansprakelijkheid voor schade, van welke aard ook, die verband houdt met risico's verbonden aan het elektronisch verzenden van berichten.

This message may contain information that is not intended for you. If you are not the addressee or if this message was sent to you by mistake, you are requested to inform the sender and delete the message. The State accepts no liability for damage of any kind resulting from the risks inherent in the electronic transmission of messages.

⚠ This symbol is automatically added to emails originating from outside of the organization. Be extra careful with hyperlinks and attachments.

ENGIE Mail Disclaimer: <http://www.engie.com/disclaimer/>

Release form, visual inspection risk class 1 asbestos removal**General data**

Company name:	Brown and Mason B.V.
Operational Manager:	
Site address:	Hollandiaweg 11
Zipcode and city:	6541 BL Nijmegen
Description of work area:	Asbestos Removal area 1 and separation between FGD and Precips.
Date:	26-2, 10-3, 11-3, 12-3, 15-3, 16-3, 17-3, 24-3, 25-3, 26-3, 30-3-2021

Registration asbestos materials risk class 1 (in accordance with asbestos survey)

Source no	Location on site	Material (application, asbestos type and asbestos percentage)	Projectnumber, Asbestos survey number
3	Zone 14 E-filters	Stamps, Chrysotiel 30-60%	Projectnumber C2002, Asbestos survey number 201314.4 V1.0 and 201314.4 V1.1
6	Zone 14 E-filters	Textile bandage Chrysotiel 60-100%	

Inspection preconditions

	Checked				Comments
Is the working area dry?	☐		☐	  irrelevant	Outside area
Is the working area visual clean?	☒		☐		
Did you find any other possible asbestos containing materials?	☒		☐		We found a part with textile bandage. Because of the condition it could be separated by cutting on both sides and remove it as RC 1

Inspection after the removal of building and construction parts where the asbestos-containing material has been used.

No	Location on site	Result				Comments
1	Asbestos removal area in front off the Precips. Asbestos Removal area 1.	☒		☐		
2	Separation area between FGD and Precips.	☒		☐		
3		☐		☐		
4		☐		☐		

5		☐	☒	☐	☒	
---	--	--------------------------	-------------------------------------	--------------------------	-------------------------------------	--

I hereby declare, as responsible person, that I have visually inspected the work area and that I have delivered it asbestos-free and clean in a responsible manner.

Supervisor asbestos(Dutch) name: 5.1.2e

Certificate nr:	04A-050319 -341592
Date: 30-3-2021	

Signature:	
------------	---

Photo attachment



Description photo: 26-2-2021 metal pieces outside the fencing after removal asbestos



Description photo: 26-2-2021 metal pieces outside the fencing after removal asbestos



Description photo: 26-2-2021 metal pieces outside the fencing after removal asbestos



Description photo: 26-2-2021 metal pieces outside the fencing after removal asbestos



Description photo: 10-3-2021 parts off separation between FGD and Precips



Description photo: 10-3-2021 parts off separation between FGD and Precips



Description photo: 10-3-2021 parts off separation between FGD and Precips



Description photo: 10-3-2021 parts off separation between FGD and Precips



Description photo: 10-3-2021 parts off separation between FGD and Precips



Description photo: 10-3-2021 parts off separation between FGD and Precips



Description photo: 10-3-2021 parts off separation between FGD and Precips



Description photo: 10-3-2021 parts off separation between FGD and Precips



Description photo: 10-3-2021 parts off separation between FGD and Precips



Description photo: 10-3-2021 parts off separation between FGD and Precips



Description photo: 10-3-2021 parts off separation between FGD and Precips



Description photo: 10-3-2021 parts off separation between FGD and Precips



Description photo: 11-3-2021 parts off separation between FGD and Precips



Description photo: 11-3-2021 parts off separation between FGD and Precips



Description photo: 11-3-2021 parts off separation between FGD and Precips



Description photo: 11-3-2021 parts off separation between FGD and Precips



Description photo: 11-3-2021 parts off separation between FGD and Precips



Description photo: 11-3-2021 parts off separation between FGD and Precips



Description photo: 12-3-2021 parts off separation between FGD and Precips



Description photo: 12-3-2021 parts off separation between FGD and Precips



Description photo: 12-3-2021 parts off separation between FGD and Precips



Description photo: 12-3-2021 parts off separation between FGD and Precips



Description photo: 12-3-2021 parts off separation between FGD and Precips



Description photo: 12-3-2021 parts off separation between FGD and Precips



Description photo: 12-3-2021 parts off separation between FGD and Precips



Description photo: 12-3-2021 parts off separation between FGD and Precips



Description photo: 15-3-2021 parts off separation between FGD and Precips



Description photo: 15-3-2021 parts off separation between FGD and Precips



Description photo: 15-3-2021 parts off separation between FGD and Precips



Description photo: 15-3-2021 parts off separation between FGD and Precips




Description photo: 15-3-2021 parts off separation between FGD and Precips



Description photo: 15-3-2021 parts off separation between FGD and Precips



Description photo: 15-3-2021 parts off separation between FGD and Precips

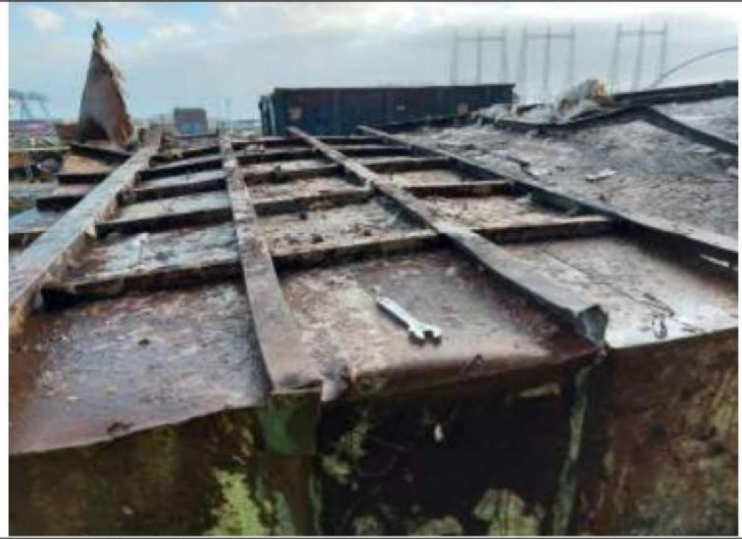

Description photo: 15-3-2021 parts off separation between FGD and Precips



Description photo: 16-3-2021 parts off separation between FGD and Precips



Description photo: 16-3-2021 parts off separation between FGD and Precips



Description photo: 16-3-2021 parts off separation between FGD and Precips



Description photo: 16-3-2021 parts off separation between FGD and Precips



Description photo: 16-3-2021 parts off separation between FGD and Precips



Description photo: 16-3-2021 parts off separation between FGD and Precips



Description photo: 16-3-2021 parts off separation between FGD and Precips



Description photo: 16-3-2021 parts off separation between FGD and Precips



Description photo: 16-3-2021 parts off separation between FGD and Precips



Description photo: 16-3-2021 parts off separation between FGD and Precips



Description photo: 17-3-2021 parts off separation between FGD and Precips



Description photo: 17-3-2021 parts off separation between FGD and Precips



Description photo: 17-3-2021 parts off separation between FGD and Precips



Description photo: 17-3-2021 parts off separation between FGD and Precips



Description photo: 17-3-2021 parts off separation between FGD and Precips



Description photo: 17-3-2021 parts off separation between FGD and Precips



Description photo: 24-3-2021 parts off separation between FGD and Precips



Description photo: 24-3-2021 parts off separation between FGD and Precips



Description photo: 24-3-2021 parts off separation between FGD and Precips



Description photo: 24-3-2021 parts off separation between FGD and Precips



Description photo: 24-3-2021 parts off separation between FGD and Precips



Description photo: 24-3-2021 parts off separation between FGD and Precips



Description photo: 24-3-2021 parts off separation between FGD and Precips



Description photo: 24-3-2021 parts off separation between FGD and Precips



Description photo: 24-3-2021 parts off separation between FGD and Precips



Description photo: 24-3-2021 parts off separation between FGD and Precips



Description photo: 25-3-2021 parts off separation between FGD and Precips




Description photo: 25-3-2021 parts off separation between FGD and Precips



Description photo: 25-3-2021 parts off separation between FGD and Precips




Description photo: 25-3-2021 parts off separation between FGD and Precips

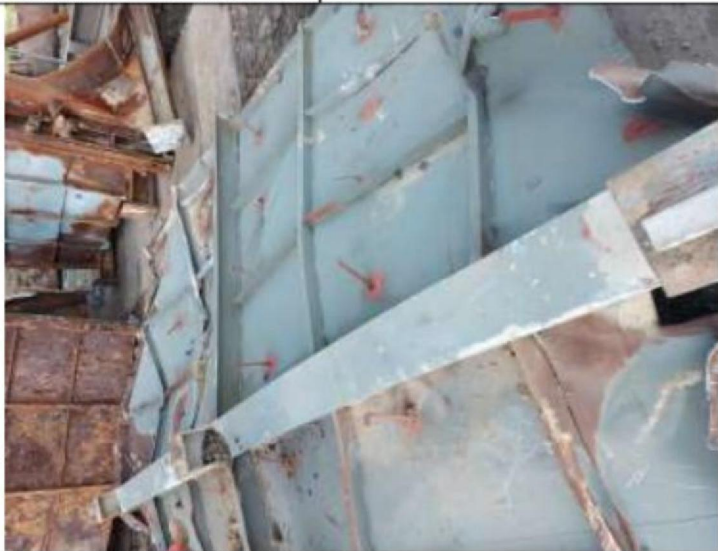

Description photo: 25-3-2021 parts off separation between FGD and Precips



Description photo: 25-3-2021 parts off separation between FGD and Precips

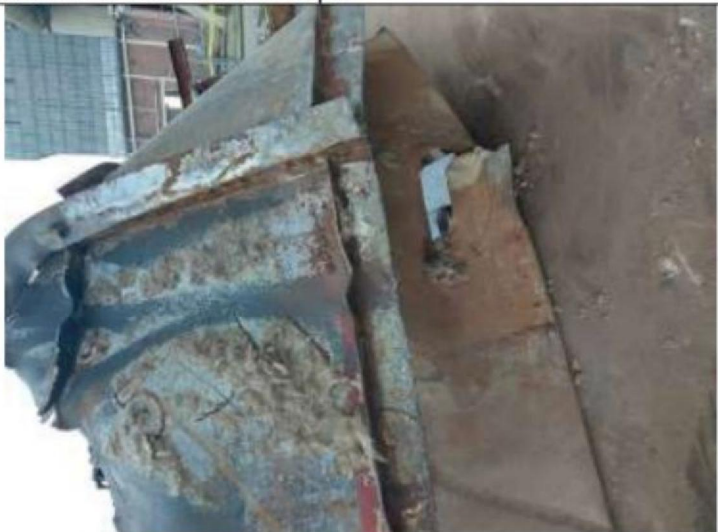

Description photo: 25-3-2021 parts off separation between FGD and Precips



Description photo: 25-3-2021 parts off separation between FGD and Precips




Description photo: 25-3-2021 parts off separation between FGD and Precips



Description photo: 25-3-2021 parts off separation between FGD and Precips



Description photo: 25-3-2021 parts off separation between FGD and Precips

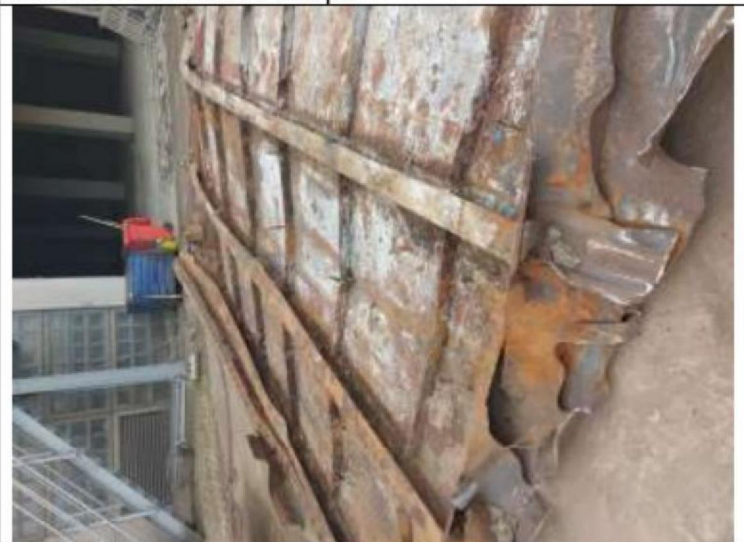

Description photo: 25-3-2021 parts off separation between FGD and Precips



Description photo: 25-3-2021 parts off separation between FGD and Precips



Description photo: 25-3-2021 parts off separation between FGD and Precips



Description photo: 26-3-2021 parts off separation between FGD and Precips



Description photo: 26-3-2021 parts off separation between FGD and Precips



Description photo: 26-3-2021 parts off separation between FGD and Precips



Description photo: 26-3-2021 parts off separation between FGD and Precips



Description photo: 26-3-2021 parts off separation between FGD and Precips



Description photo: 26-3-2021 parts off separation between FGD and Precips



Description photo: 26-3-2021 parts off separation between FGD and Precips



Description photo: 26-3-2021 parts off separation between FGD and Precips



Description photo: 26-3-2021 parts off separation between FGD and Precips. This parts includes textile bandage which has to be separated.



Description photo: 26-3-2021 parts off separation between FGD and Precips. This parts includes textile bandage which has to be separated.




Description photo: 26-3-2021 parts off separation between FGD and Precips. This parts includes textile bandage which has been separated in RC 1. After separation is has been put in the skip which has been provided with a containerbag with A-vignette.




Description photo: 26-3-2021 parts off separation between FGD and Precips. This parts includes textile bandage which has been separated in RC 1. After separation is has been put in the skip which has been provided with a containerbag with A-vignette.

Comments:

The parts of ducts and piping has been removed according to the MSD005. After removing we put the ducts and piping in the asbestos removal area 1. There the stamps have been removed and placed in asbestos A-vignet bags. The bags have been placed in a skip with a asbestos A-vignet containerbag.

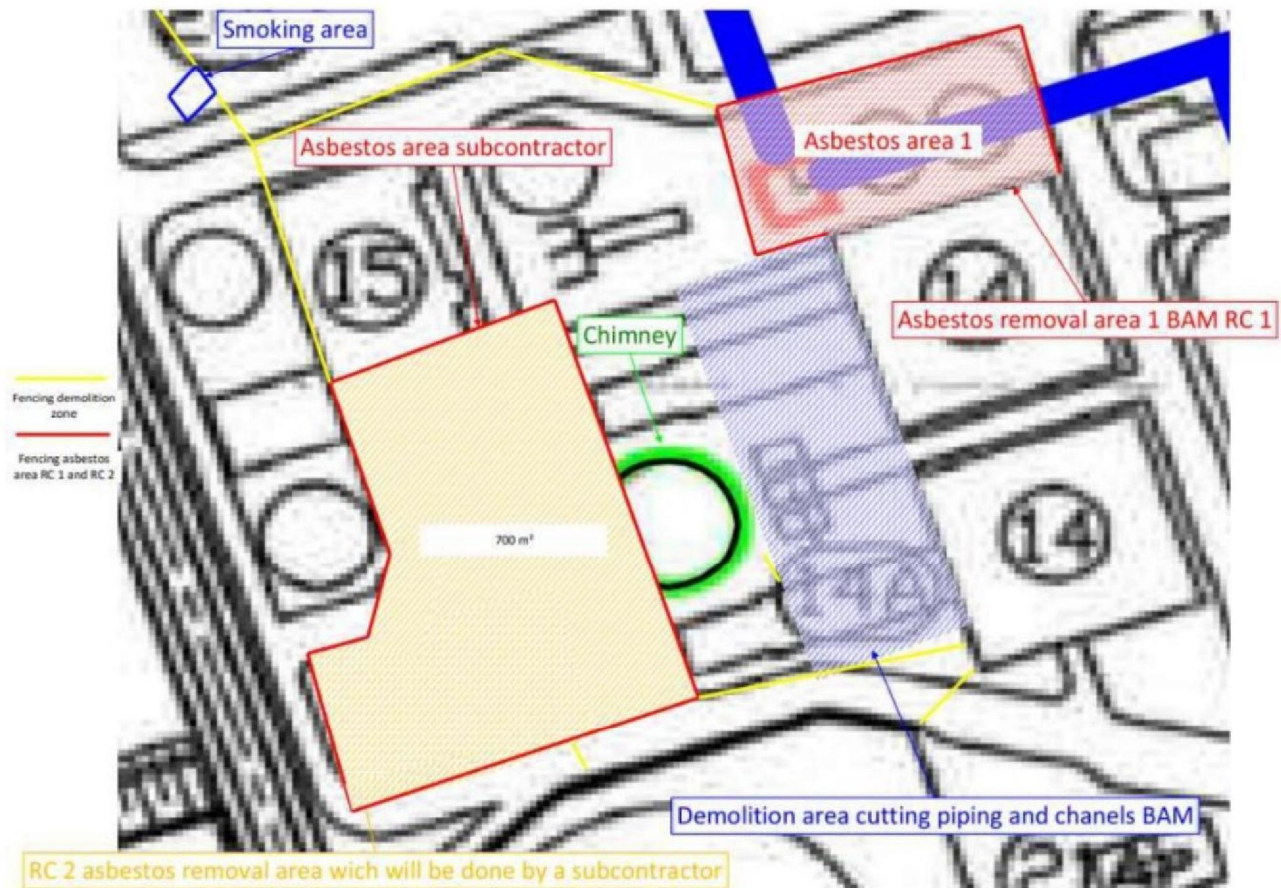Drawing asbestos area 1 and separation area

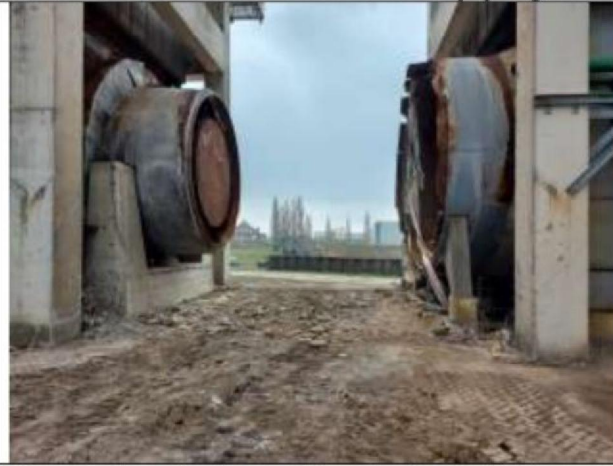Pictures after removal ducts and piping in the separation area


Description photo: position ducts and piping after removal.



Description photo: position ducts and piping after removal.



Description photo: position ducts and piping after removal.

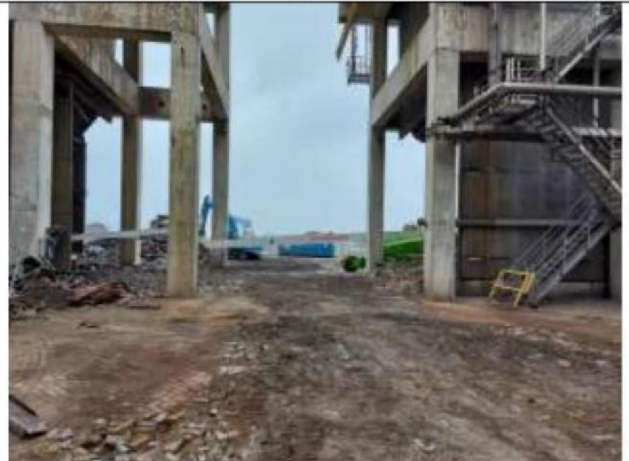

Description photo: position ducts and piping after removal.



Description photo: position ducts and piping after removal.



Description photo: position ducts and piping after removal.




Description photo: position ducts and piping after removal.



Description photo: position ducts and piping after removal.



Description photo: clean concrete floor after removed the asbestos stamps and textile bandage

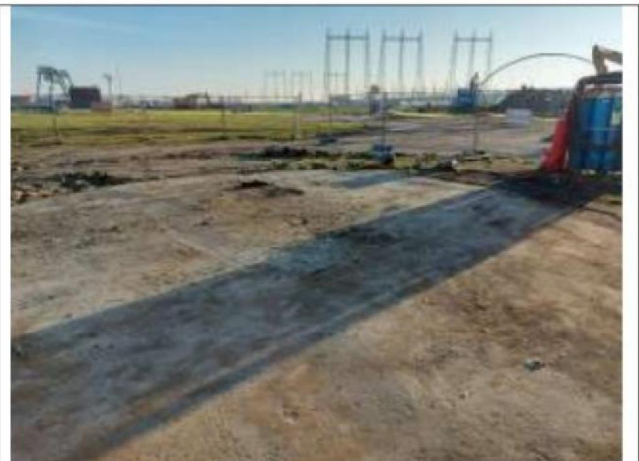

Description photo: clean concrete floor after removed the asbestos stamps and textile bandage
